



Retail Market Design Service

RMDS – Update

27th September 2023








V13.6 update

V13.6 Minor Market Release cutover complete.

- V13.6a (MCC02 meters and MCC03 Cohort 1):
 - Smart Meter Deployment commenced from 25/09/2023
 - Hypercare in place until 01/12/2023

- V13.6b (3-phase meters):
 - Testing is delayed. Impact currently being assessed.

v14.00.00 Release – Status

MCR	Version	Description	Completed Milestones	Status
1189	7.0	Additional code in the 017MM to select a de-energisation with a service removal	Schema Draft 2 released	
1209	7.0	Annual Consumption for HH Sites	Schema Draft 2 released	
1216	6.0	Smart Metering Remote Operations	Schema Draft 2 released	
1219	5.0	SPAYG System and Process changes necessary to deliver policy	Schema Draft 2 released	
1208	2.0	Smart Metering Default Data	None. Delivery blocked, dependant on the Smart Metering Data Access Code	
1221	2.0	Contingency Process for Failure in SPAYG Technology Chain	MCR Baselined	
1222	1.1	SPAYG – CTF Algorithm Suitability for SPAYG Service Provision	Delivered	


Note:

- As communicated through ILG and SSG, a small number of v14.00.00 design specs were more complex to close out than forecast. Timeline for design is extended to 22/9/23.
- Build and FUT timelines are extended.
- ESNB's view is that this will not impact on Go-Live as delay is absorbed within system integration testing.

Upcoming Milestones this Month:

None.

v14.00.00 Release – Plan

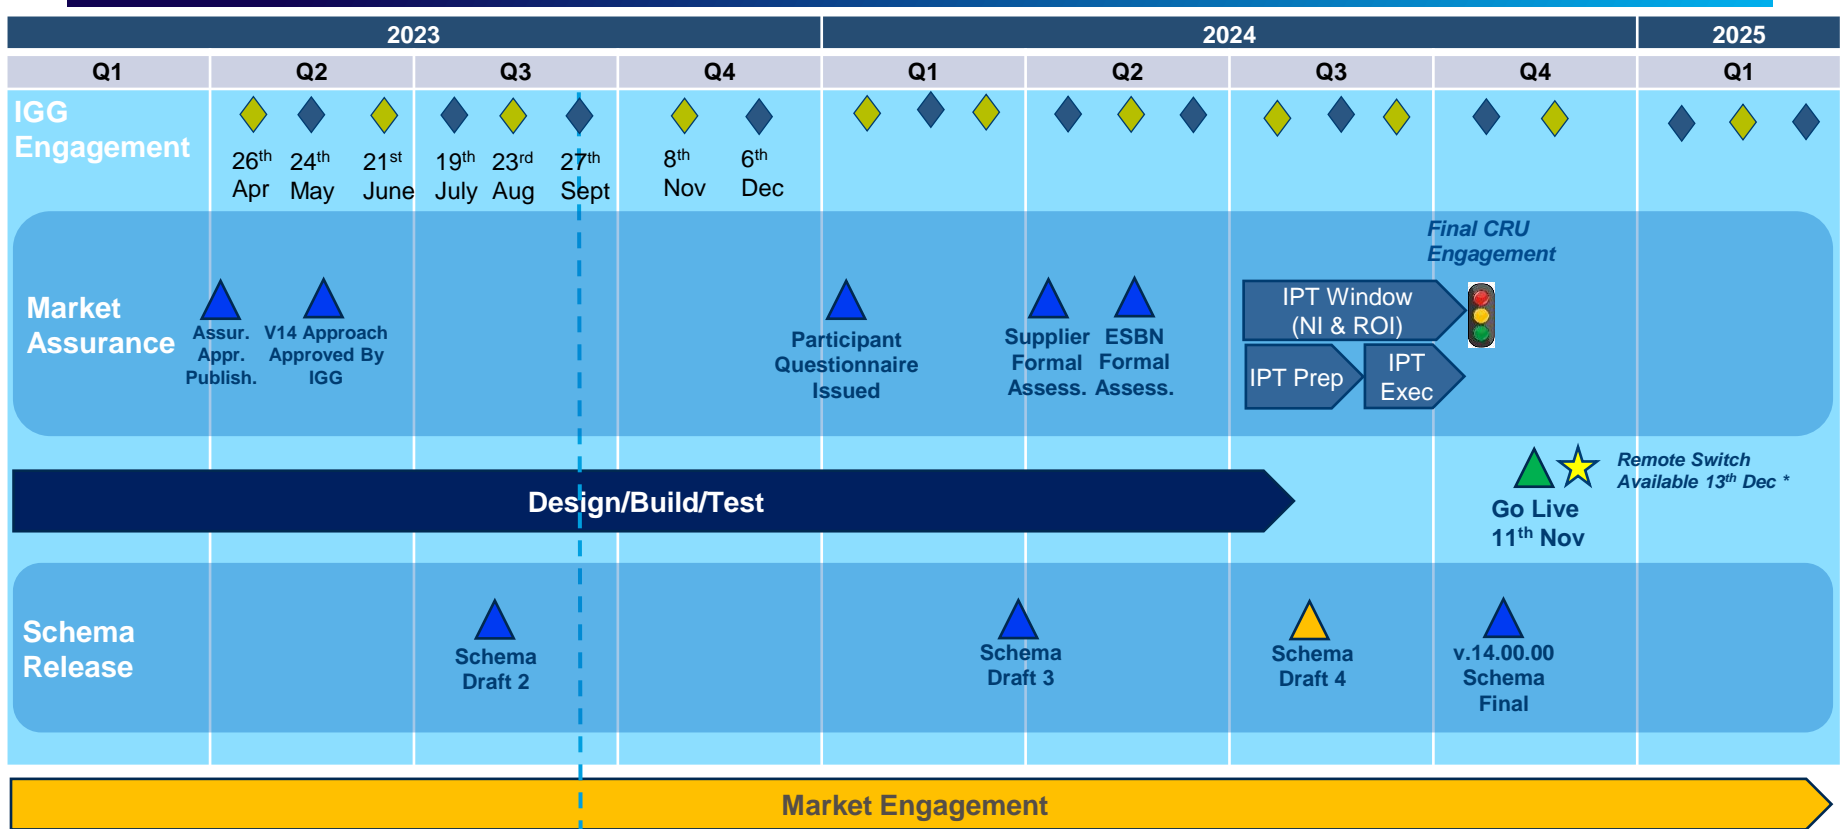

Sept 2023

*Post Activation of Firmware Switch on SEMs

Key

- ▲ ▲ IGG (Meetings & Calls)
- ◆ ◆ Key Milestone (Confirmed & Draft)
- ▲ Go live



Retail Market Design Service

Thank You
