



NETWORKS

Market Release v14.00.00 Cutover Roadmap


May 2024



- This pack describes the cutover roadmap for Market Release v14.00.00
- This release is due to go live in November 2024 under phase 2 of NSMP
- Several agreed Schema and Non-Schema changes will be delivered in this release (see *Appendix A*)
- Timely and effective collaboration is required between ESBN, Market Participants, Version1 and RMDS to ensure success of IPT and cutover timelines
- Market Participants are expected to be ready to make any necessary changes on their own systems

Cutover Roadmap

Cutover Roadmap

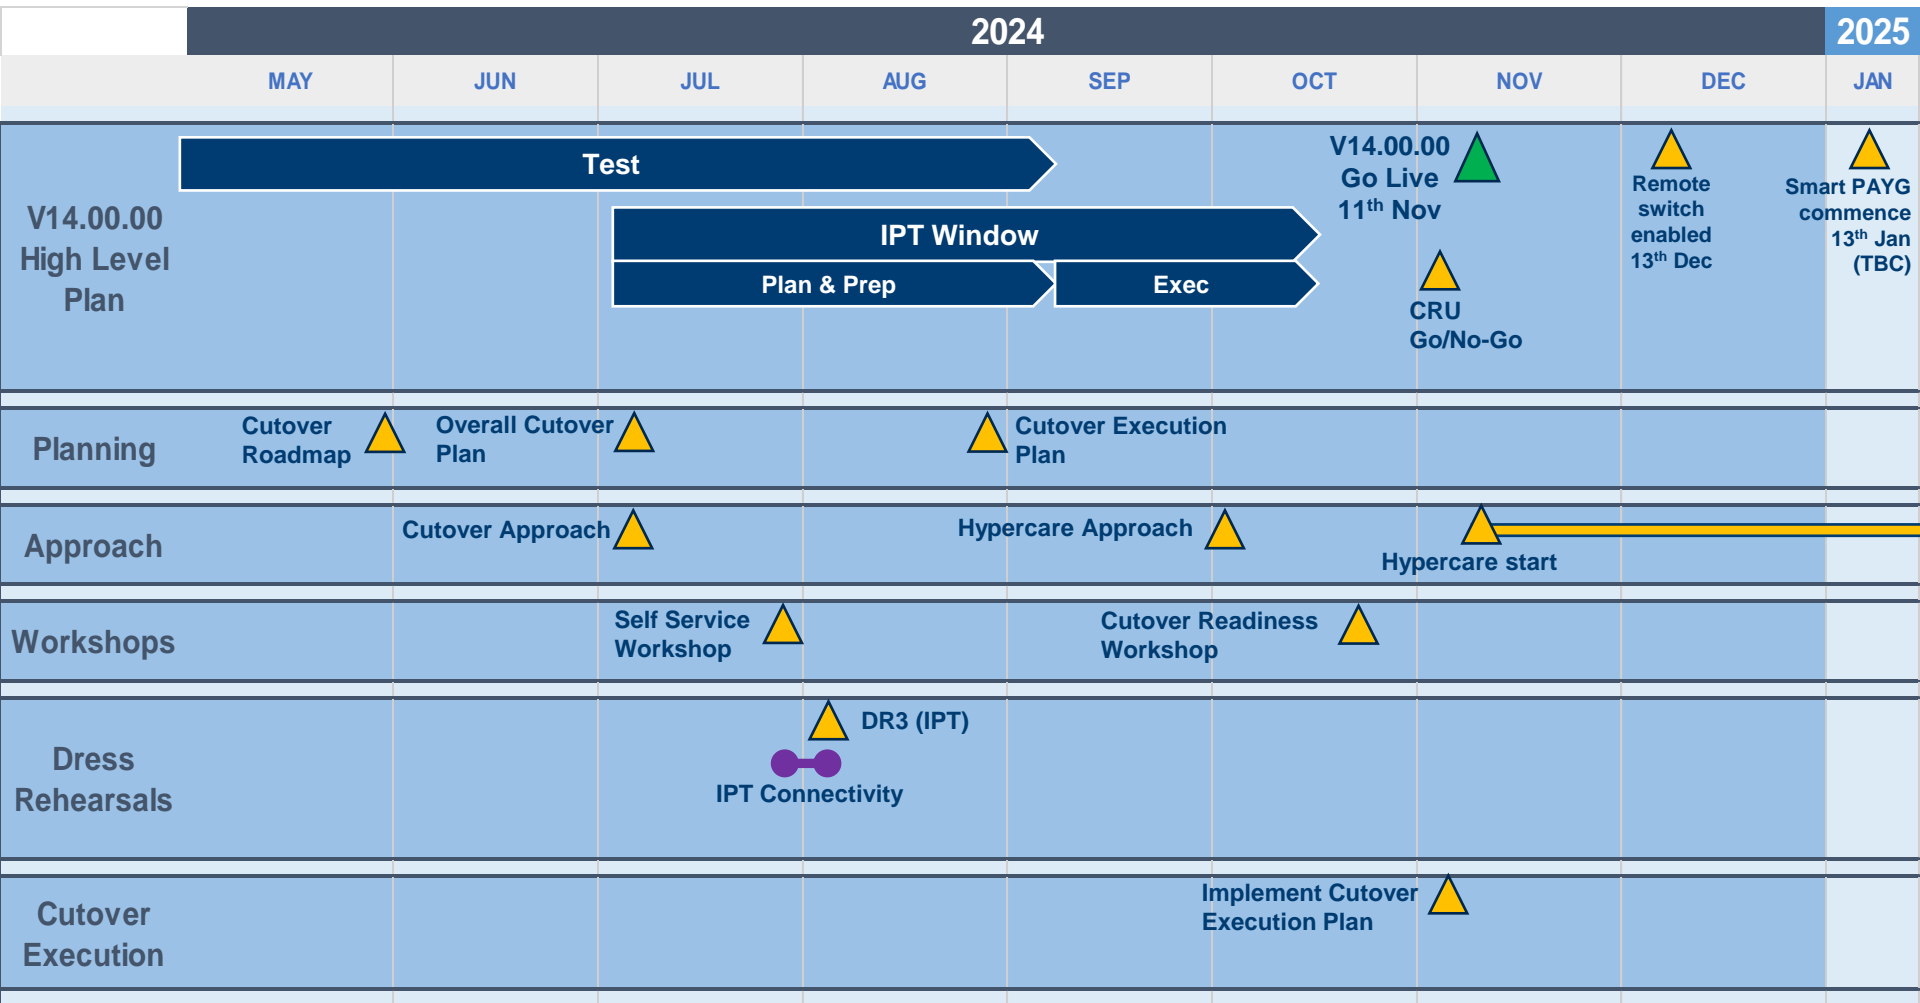

Cutover Roadmap



Date	Milestone	Notes	Impacts	Type
31 May 2024	Cutover Roadmap	<ul style="list-style-type: none">Roadmap for v14.00.00 cutover	<ul style="list-style-type: none">Market Participants	<ul style="list-style-type: none">Document
08 Jul 2024	Cutover Approach	<ul style="list-style-type: none">Approach to v14.00.00 cutover	<ul style="list-style-type: none">Market Participants	<ul style="list-style-type: none">Document
08 Jul 2024	Overall Cutover Plan	<ul style="list-style-type: none">Plan with high level dates for activities and documents in Cutover roadmap	<ul style="list-style-type: none">Market Participants	<ul style="list-style-type: none">Document
29 Jul 2024	Self-Service Workshop	<ul style="list-style-type: none">Workshop with Retail Market Participants to walk through the 'self-service' approach for v14.00.00 schema deploymentAttendance mandatoryDates to be confirmed in Overall Cutover Plan	<ul style="list-style-type: none">Market Participants	<ul style="list-style-type: none">Activity

Cutover Roadmap



Date	Milestone	Notes	Impacts	Type
06 Aug 2024	Dress Rehearsal 3 (IPT)	<ul style="list-style-type: none"> Dress Rehearsal (practicing deployment steps) in advance of IPT execution, allowing suppliers to deploy v14.00.00 schema on their IPT Test systems 4 weeks before IPT execution 	<ul style="list-style-type: none"> Market Participants 	<ul style="list-style-type: none"> Activity
30 Aug 2024	Cutover Execution Plan	<ul style="list-style-type: none"> Plan with key market tasks with dates/timings for cutover execution 	<ul style="list-style-type: none"> Market Participants 	<ul style="list-style-type: none"> Document
Wk1 Oct 2024 TBC	Hypercare Approach	<ul style="list-style-type: none"> Approach to describe the period post go live Dates to be confirmed in Cutover Execution Plan 	<ul style="list-style-type: none"> Market Participants 	<ul style="list-style-type: none"> Document
24 Oct 2024	Retail Market Participants Cutover Readiness Workshop	<ul style="list-style-type: none"> Workshop to walkthrough cutover activities and assess entry criteria Dates to be confirmed in Cutover Execution Plan 	<ul style="list-style-type: none"> Market Participants 	<ul style="list-style-type: none"> Activity
08 Nov 2024	Implement Cutover Execution Plan	<ul style="list-style-type: none"> Cutover Execution for v14.00.00 	<ul style="list-style-type: none"> Market Participants 	<ul style="list-style-type: none"> Document
11 Nov 2024	Hypercare commences	<ul style="list-style-type: none"> Hypercare for v14.00.00 commences End 14 April 2024 	<ul style="list-style-type: none"> Market Participants 	<ul style="list-style-type: none"> Activity

Appendices

Appendix A

The following Schema and non-Schema MCRs will be delivered in Market Release v14.00.00

MCR	Description
MCR1189	Removal of Service Safety Incident (additional code in the 017MM)
MCR1193	New 603MM Daily Summary Transaction Details
MCR1209	Estimated Annual Consumption for HH Sites (enduring solution)
MCR1216	Smart PAYG – Remote Operations
MCR1219	Smart PAYG – System & Process Changes
MCR1221	Smart PAYG – Contingency Process
